SAFFRON WALDEN COUNTY HIGH SCHOOL - PROPOSED 3G PITCH & CAR PARK

CONTRACT PROGRAMME OF WORKS
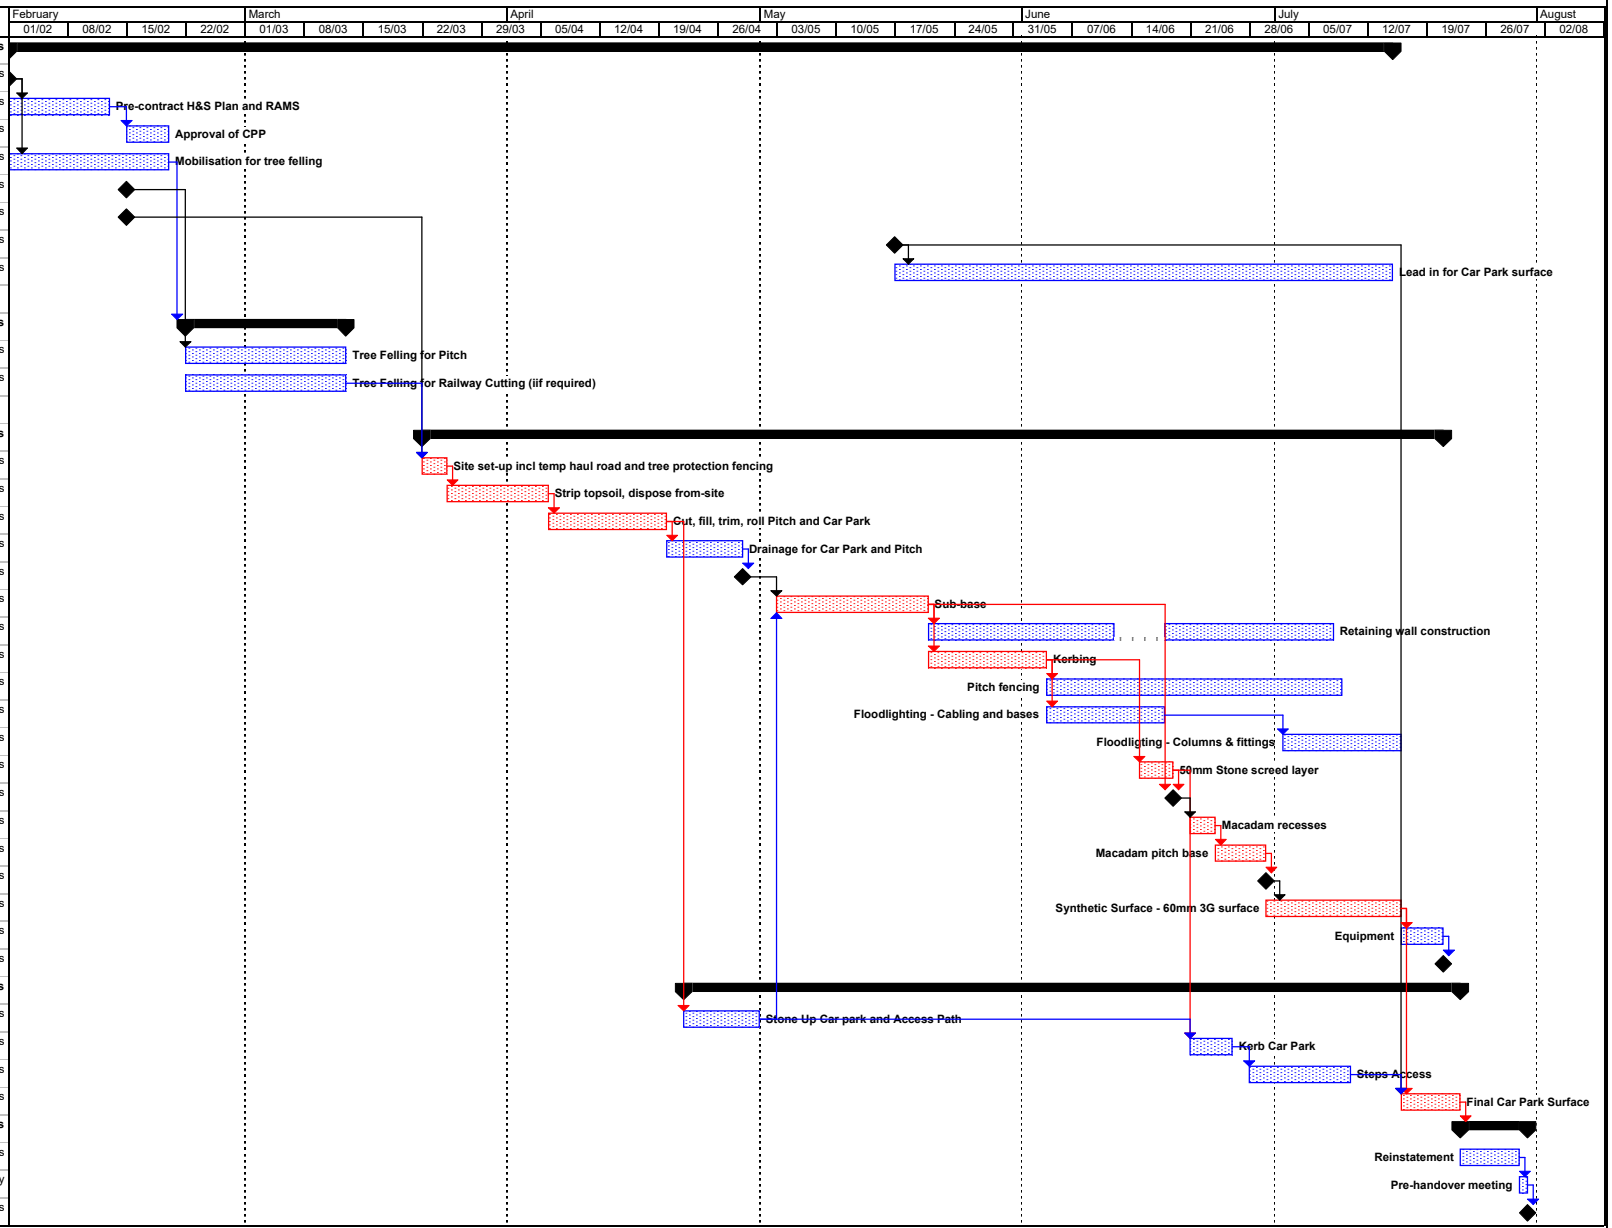
ID	Task Name	Duration
1	**Lead-in**	**118 days**
2	**Receipt of official order**	0 days
3	Pre-contract H&S Plan and RAMS	10 days
4	Approval of CPP	5 days
5	Mobilisation for tree felling	15 days
6	Landscaping/Tress Discharge Milestone	0 days
7	Confirmation of Topsoil Location	0 days
8	Confirmation date of Car Park surface	0 days
9	Lead in for Car Park surface	43 days
10		
11	**Enabling Works**	**15 days**
12	Tree Felling for Pitch	15 days
13	Tree Felling for Railway Cutting (iif required)	15 days
14		
15	**AGP**	**87 days**
16	Site set-up incl temp haul road and tree protection fencing	3 days
17	Strip topsoil, dispose from-site	8 days
18	Cut, fill, trim, roll Pitch and Car Park	10 days
19	Drainage for Car Park and Pitch	7 days
20	**Key Stage Inspection - Formation and Drainage**	0 days
21	Sub-base	14 days
22	Retaining wall construction	30 days
23	Kerbing	10 days
24	Pitch fencing	25 days
25	Floodlighting - Cabling and bases	10 days
26	Floodligting - Columns & fittings	10 days
27	50mm Stone screed layer	4 days
28	**Key Stage Inspection - Sub-base**	0 days
29	Macadam recesses	3 days
30	Macadam pitch base	4 days
31	**Key Stage Inspection - Macadam pitch base**	0 days
32	Synthetic Surface - 60mm 3G surface	12 days
33	Equipment	3 days
34	**Fianl Key Stage Inspection**	0 days
35	**Car Park**	**66 days**
36	Stone Up Car park and Access Path	7 days
37	Kerb Car Park	5 days
38	Steps Access	10 days
39	Final Car Park Surface	5 days
40	**Finishings**	**6 days**
41	Reinstatement	5 days
42	Pre-handover meeting	1 day
43	**Handover**	0 days
