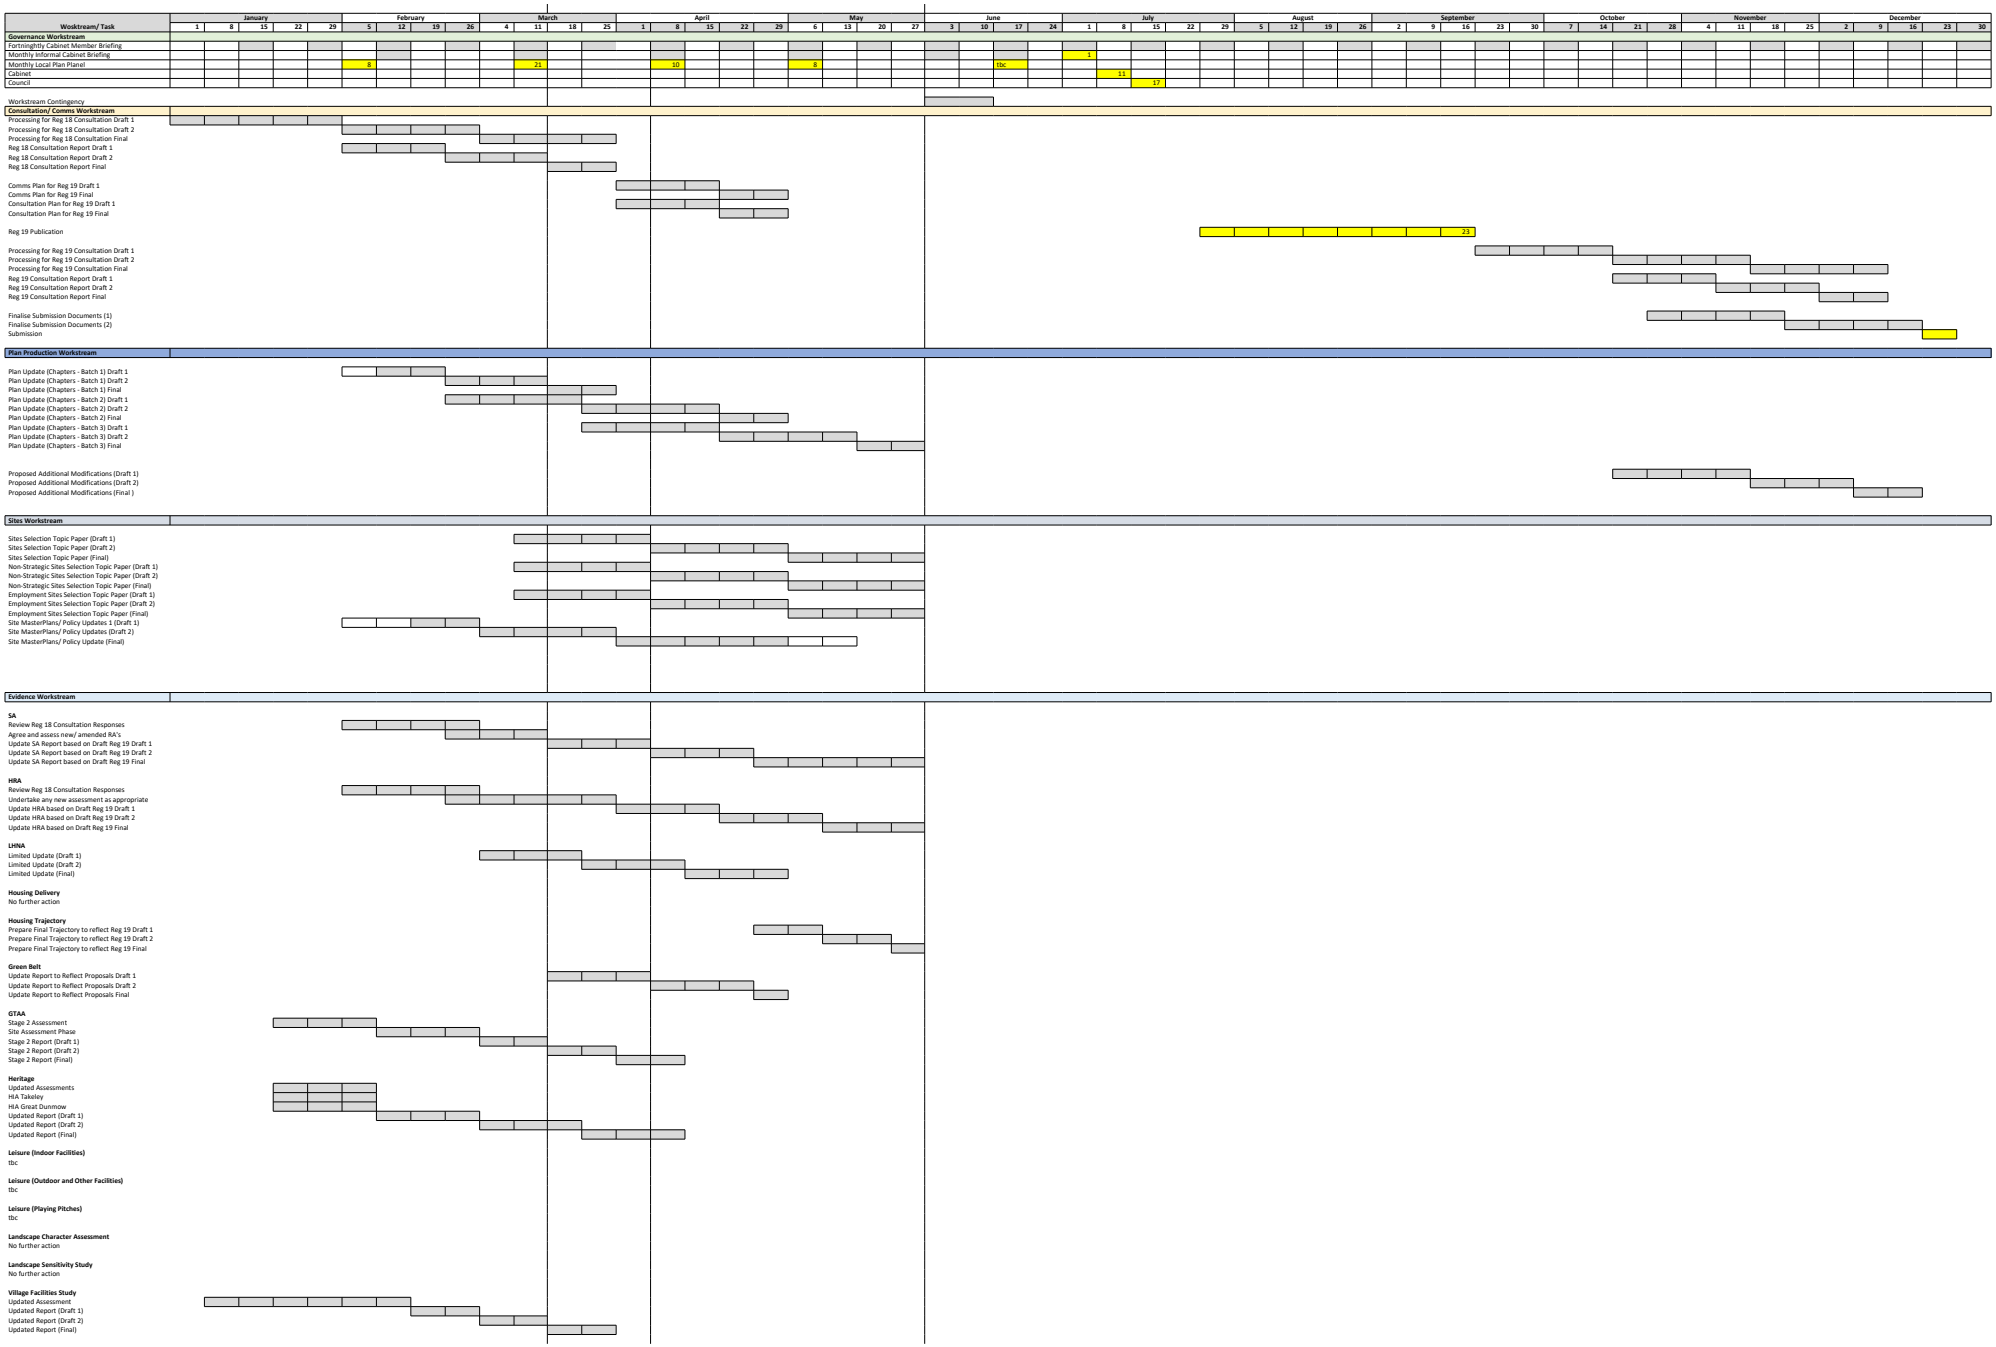
Wokstream/ Task
January
February
March
April
May
June
July
August
September
October
November
December
1 8 15 22 29 5 12 19 26 4 11 18 25 1 8 15 22 29 6 13 20 27 3 10 17 24 1 8 15 22 29 5 12 19 26 2 9 16 23 30 7 14 21 28 4 11 18 25 2 9 16 23 30
Governance Workstream
Fortnnightly Cabinet Member Briefing
Monthly Informal Cabinet Briefing
Monthly Local Plan Planel
Cabinet
Council
8
21
10
8
tbc
11
17
Workstream Contingency
Consultation/ Comms Workstream
Processing for Reg 18 Consultation Draft 1
Processing for Reg 18 Consultation Draft 2
Processing for Reg 18 Consultation Final
Reg 18 Consultation Report Draft 1
Reg 18 Consultation Report Draft 2
Reg 18 Consultation Report Final
Comms Plan for Reg 19 Draft 1
Comms Plan for Reg 19 Final
Consultation Plan for Reg 19 Draft 1
Consultation Plan for Reg 19 Final
Reg 19 Publication
23
Processing for Reg 19 Consultation Draft 1
Processing for Reg 19 Consultation Draft 2
Processing for Reg 19 Consultation Final
Reg 19 Consultation Report Draft 1
Reg 19 Consultation Report Draft 2
Reg 19 Consultation Report Final
Finalise Submission Documents (1)
Finalise Submission Documents (2)
Submission
Plan Production Workstream
Plan Update (Chapters - Batch 1) Draft 1
Plan Update (Chapters - Batch 1) Draft 2
Plan Update (Chapters - Batch 1) Final
Plan Update (Chapters - Batch 2) Draft 1
Plan Update (Chapters - Batch 2) Draft 2
Plan Update (Chapters - Batch 2) Final
Plan Update (Chapters - Batch 3) Draft 1
Plan Update (Chapters - Batch 3) Draft 2
Plan Update (Chapters - Batch 3) Final
Proposed Additional Modifications (Draft 1)
Proposed Additional Modifications (Draft 2)
Proposed Additional Modifications (Final)
Sites Workstream
Sites Selection Topic Paper (Draft 1)
Sites Selection Topic Paper (Draft 2)
Sites Selection Topic Paper (Final)
Non-Strategic Sites Selection Topic Paper (Draft 1)
Non-Strategic Sites Selection Topic Paper (Draft 2)
Non-Strategic Sites Selection Topic Paper (Final)
Employment Sites Selection Topic Paper (Draft 1)
Employment Sites Selection Topic Paper (Draft 2)
Employment Sites Selection Topic Paper (Final)
Site MasterPlans/ Policy Updates 1 (Draft 1)
Site MasterPlans/ Policy Updates (Draft 2)
Site MasterPlans/ Policy Update (Final)
Evidence Workstream
SA
Review Reg 18 Consultation Responses
Agree and assess new/ amended RA's
Update SA Report based on Draft Reg 19 Draft 1
Update SA Report based on Draft Reg 19 Draft 2
Update SA Report based on Draft Reg 19 Final
HRA
Review Reg 18 Consultation Responses
Undertake any new assessment as appropriate
Update HRA based on Draft Reg 19 Draft 1
Update HRA based on Draft Reg 19 Draft 2
Update HRA based on Draft Reg 19 Final
LHNA
Limited Update (Draft 1)
Limited Update (Draft 2)
Limited Update (Final)
Housing Delivery
No further action
Housing Trajectory
Prepare Final Trajectory to reflect Reg 19 Draft 1
Prepare Final Trajectory to reflect Reg 19 Draft 2
Prepare Final Trajectory to reflect Reg 19 Final
Green Belt
Update Report to Reflect Proposals Draft 1
Update Report to Reflect Proposals Draft 2
Update Report to Reflect Proposals Final
GTAA
Stage 2 Assessment
Site Assessment Phase
Stage 2 Report (Draft 1)
Stage 2 Report (Draft 2)
Stage 2 Report (Final)
Heritage
Updated Assessments
HIA Takeley
HIA Great Dunmow
Updated Report (Draft 1)
Updated Report (Draft 2)
Updated Report (Final)
Leisure (Indoor Facilities)
tbc
Leisure (Outdoor and Other Facilities)
tbc
Leisure (Playing Pitches)
tbc
Landscape Character Assessment
No further action
Landscape Sensitivity Study
No further action
Village Facilities Study
Updated Assessment
Updated Report (Draft 1)
Updated Report (Draft 2)
Updated Report (Final)

Climate Change Study
Updated Report (Draft 1)
Updated Report (Draft 2)
Updated Report (Final)

GBI Strategy
No further action

Country Parks / SANG Work
Report (Draft 1)
Report (Draft 2)
Report (Final)

Viability Study
Updated Report (Draft 1)
Updated Report (Draft 2)
Updated Report (Final)

Biodiversity Net Gain
tbc

Economic Needs Assessment
Limited Update (Draft 1)
Limited Update (Draft 2)
Limited Update (Final)

Employment Land Review
Report (Draft 1)
Report (Draft 2)
Report (Final)

Retail Study
Limited Update (Draft 1)
Limited Update (Draft 2)
Limited Update (Final)

Villages Housing Requirement
Limited Update (Draft 1)
Limited Update (Draft 2)
Limited Update (Final)

IDP
Updated Report (Draft 1)
Updated Report (Draft 2)
Updated Report (Final)

HELAA
Updated Report (Draft 1)
Updated Report (Draft 2)
Updated Report (Final)

Water Cycle Study
Updated Report (Draft 1)
Updated Report (Draft 2)
Updated Report (Final)

SFRA
Updated Report (Draft 1)
Updated Report (Draft 2)
Updated Report (Final)

Air Quality
No further action

Transport Modelling
Interim Outputs
Updated Report (Draft 1)
Updated Report (Draft 2)
Updated Report (Final)
Add Others

A120 Study
tbc (ECC leading)

LCWIP
Final Report

Transport Topic Paper
Updated Report (Draft 1)
Updated Report (Draft 2)
Updated Report (Final)

DTC Workstream

SOCG Tranche 1 (Draft 1)
SOCG Tranche 1 (Draft 2)
SOCG Tranche 1 (Final)
SOCG Tranche 2 (Draft 1)
SOCG Tranche 2 (Draft 2)
SOCG Tranche 2 (Final)
